

## Project Planning Phase

### Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

|               |                                                |
|---------------|------------------------------------------------|
| Date          | 29 September 2026                              |
| Team ID       | SWTID-2026-8263                                |
| Project Name  | Import Data using Transform Maps (Spreadsheet) |
| Maximum Marks | 5 Marks                                        |

#### Product Backlog, Sprint Schedule, and Estimation (4 Marks)

| Sprint   | Functional Requirement (Epic)    | User Story Number | User Story / Task                                                                                    | Story Points | Priority | Team Members |
|----------|----------------------------------|-------------------|------------------------------------------------------------------------------------------------------|--------------|----------|--------------|
| Sprint-1 | Data Collection & Table Creation | USN-1             | As an admin, I can create a spreadsheet of employee details (ID, Name, Email, Department, Location). | 2            | High     |              |
| Sprint-1 |                                  | USN-2             | As an admin, I can create the target Employee table in ServiceNow.                                   | 2            | High     |              |
| Sprint-1 | Import Set & Transform Map       | USN-3             | As an admin, I can create an Import Set table to stage the spreadsheet data.                         | 3            | High     |              |
| Sprint-1 |                                  | USN-4             | As an admin, I can create a Transform Map to map import fields to the Employee table.                | 3            | High     |              |
| Sprint-1 | Transform & Validate             | USN-5             | As an admin, I can transform and validate the imported employee data.                                | 2            | Medium   |              |
| Sprint-2 | Data Integrity (Coalesce)        | USN-6             | As an admin, I can enable Coalesce on Employee ID to avoid duplicate records.                        | 3            | High     |              |
| Sprint-2 |                                  | USN-7             | As an admin, I can insert/update employee data from an Excel file through the transform.             | 2            | Medium   |              |
| Sprint-2 | Reports                          | USN-8             | As a user, I can view an Employee List report.                                                       | 2            | Medium   |              |
| Sprint-2 |                                  | USN-9             | As a user, I can view Employees by Location as a bar chart.                                          | 2            | Low      |              |
| Sprint-2 |                                  | USN-10            | As a user, I can view Employees by Department as a pie chart.                                        | 2            | Low      |              |
| Sprint-2 | Dashboard                        | USN-11            | As a user, I can view all reports together on a single dashboard.                                    | 5            | High     |              |

**Sprint-1 total = 2 + 2 + 3 + 3 + 2 = 12** | **Sprint-2 total = 3 + 2 + 2 + 2 + 2 + 5 = 16**

#### Project Tracker, Velocity & Burndown Chart (4 Marks)

| Sprint   | Total Story Points | Duration | Sprint Start Date | Sprint End Date (Planned) | Story Points Completed (Planned End Date) | Sprint Release Date (Actual) |
|----------|--------------------|----------|-------------------|---------------------------|-------------------------------------------|------------------------------|
| Sprint-1 | 12                 | 6 Days   | 22 Sep 2026       | 27 Sep 2026               | 12                                        | 27 Sep 2026                  |
| Sprint-2 | 16                 | 6 Days   | 29 Sep 2026       | 04 Oct 2026               | 16                                        | 04 Oct 2026                  |

#### Velocity:


Our sprint duration is 6 days and the team's velocity is 14 story points per sprint. The average velocity (AV) per day is the story points delivered per working day:

$$AV = \text{velocity} \div \text{sprint duration} = 14 \div 6 \approx 2.3 \text{ story points per day}$$

*Note: velocity per day = velocity ÷ sprint duration (story points delivered per day). In the original sample the label read "sprint duration ÷ velocity" but the numbers used velocity ÷ duration (20 ÷ 10 = 2), so the formula above is the corrected version.*

#### Burndown Chart:

A burndown chart is a graphical representation of work left to do versus time. It is often used in agile software development methodologies such as Scrum, but can be applied to any project containing measurable progress over time. The chart below tracks the remaining story points across our two sprints against the ideal burndown line.

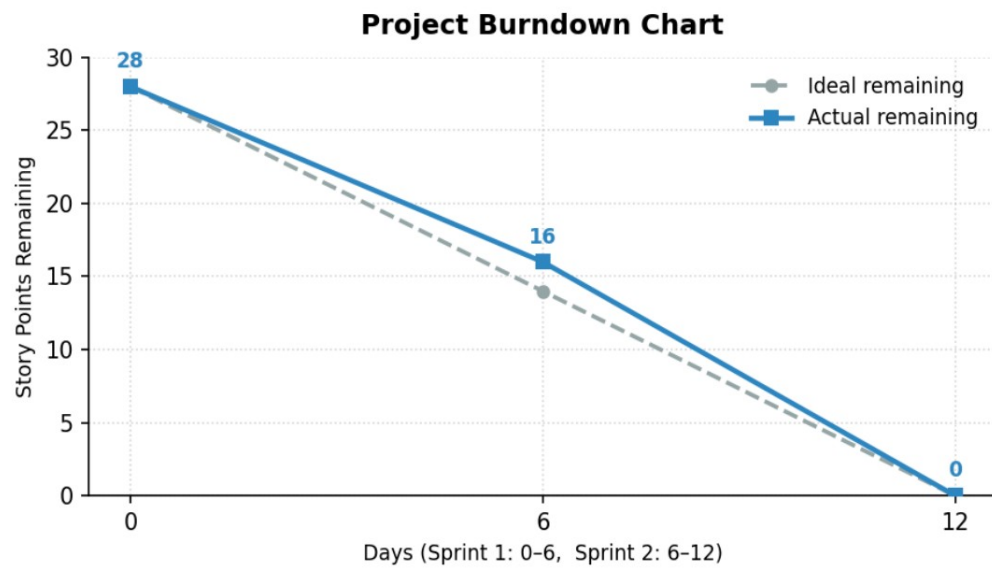

**Reference:**

<https://www.atlassian.com/agile/project-management>  
<https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software>  
<https://www.atlassian.com/agile/tutorials/epics>  
<https://www.atlassian.com/agile/tutorials/sprints>  
<https://www.atlassian.com/agile/project-management/estimation>  
<https://www.atlassian.com/agile/tutorials/burndown-charts>
